

Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 25

Construction Progress Report

Monthly Period Reporting

Start: Monday, 01 April 2024 End: Tuesday, 31 April 2024

Builder

NS Reformas, Construccion Y Trading S.L.U

Current Process

Description of work

1. Continue painting
2. Level floors
3. Waterproof the bathrooms

Process Photos











Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 25

In April, the builders diligently continued treating and filling the joints of the walls and ceilings on the 1st, 2nd, and 3rd floors. Following this, they proceeded with painting the walls and ceilings white in both the apartments and the common staircase.

Additionally, they began working on the flooring, leveling the surfaces in preparation for the final pavement installation.

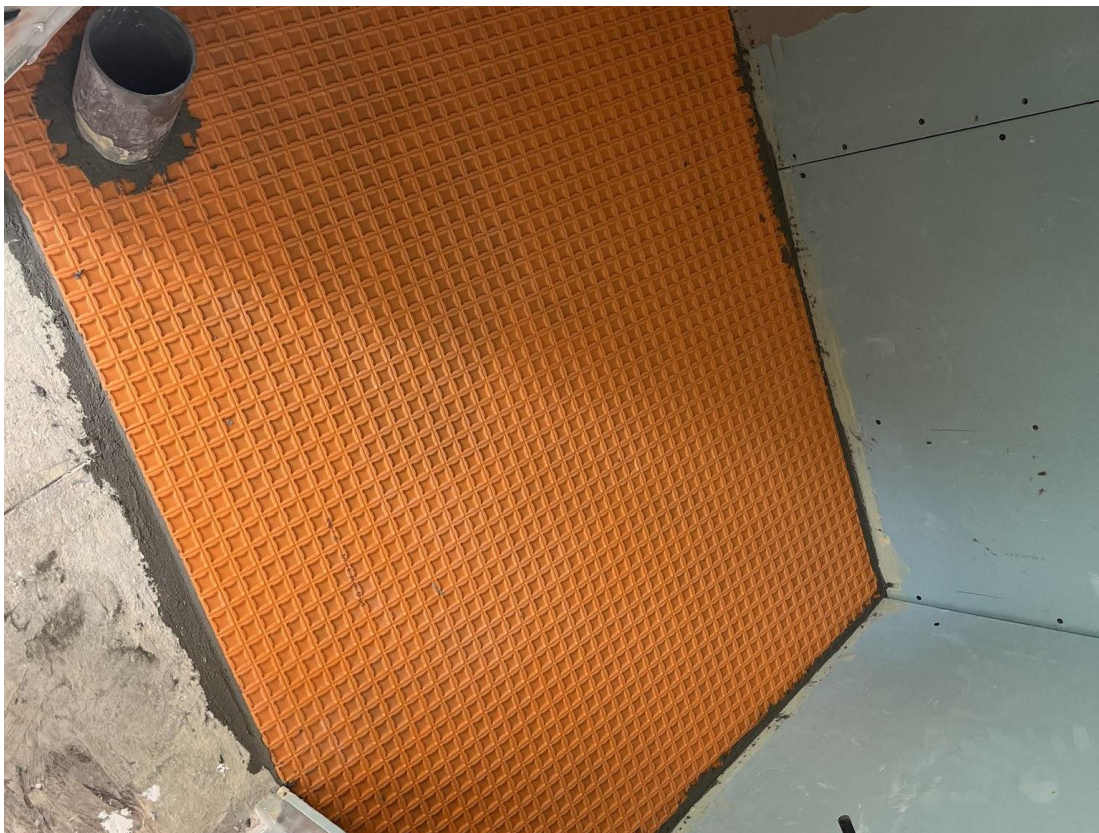

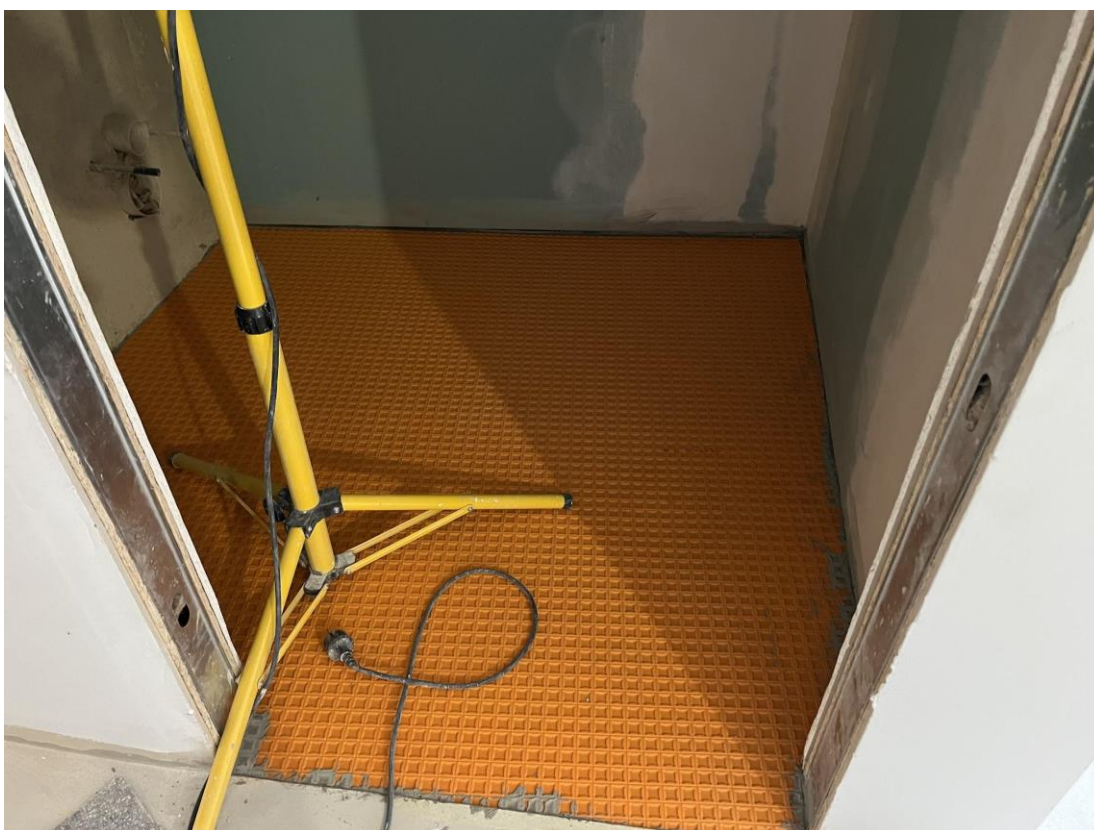

Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 25



Meanwhile, the builders began applying waterproofing to the bathroom areas of the apartments above the ground floor, meticulously preparing them for the upcoming tiling phase.
