

**Project:** Rua Nova do Loureiro 43-45, Lisboa

**Report Number:** Laurel - 27



**YAO TENG FGI**  
Property Development

## Construction Progress Report

**Monthly Period Reporting**

Start: Wednesday, 01 May 2024    End: Friday, 31 May 2024

**Builder**

LADRILLO S.A - Construção, Remediações e Projecto


### Current Process


**Description of work**

1. Zinc cladding
2. Insulation placing
3. Building infrastructure work

### Process Photos



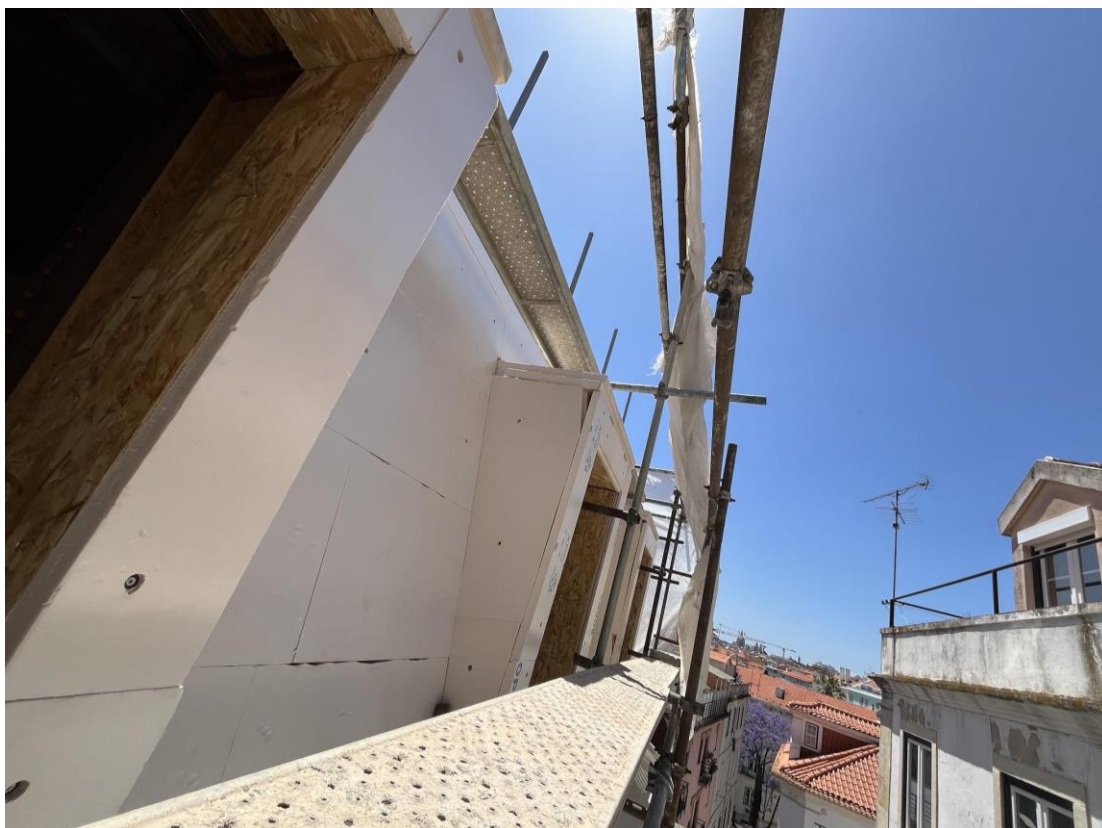

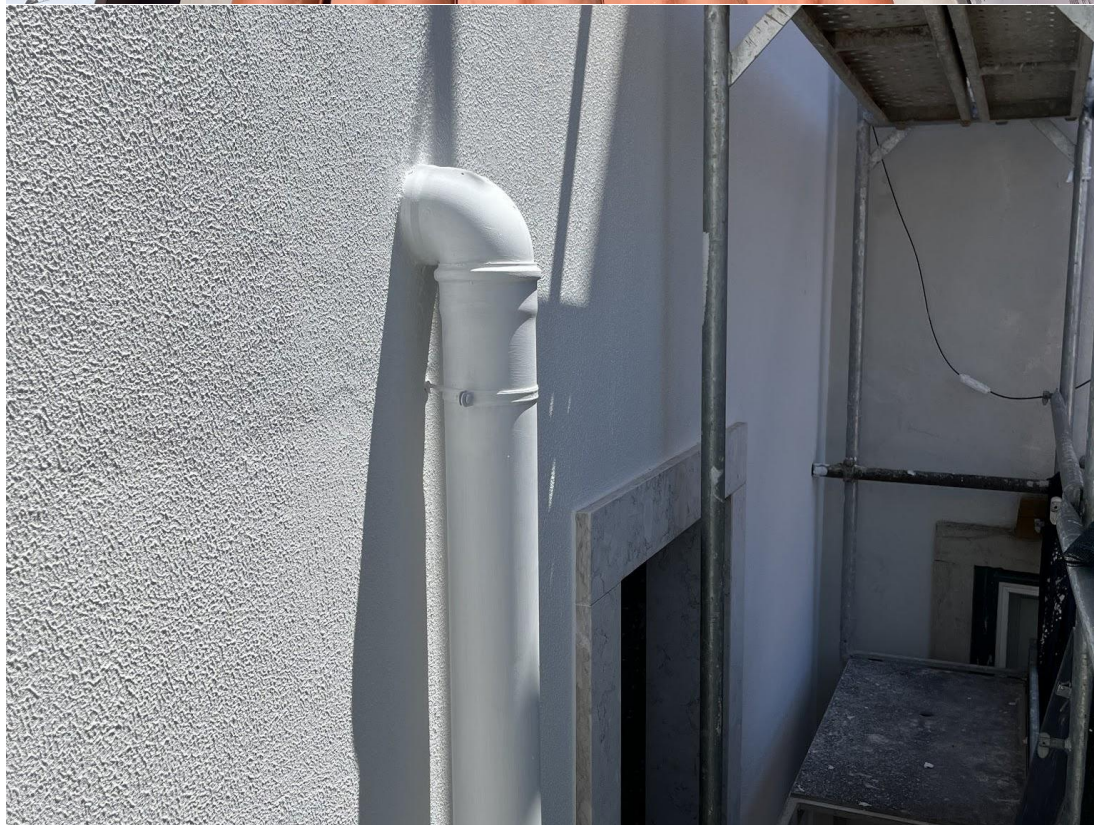


**In May, the builders continued with zinc cladding of the roof. After completing the zinc covering and roof tiling on the side that facing the garden, they started painting the facade the facade wall white. Simultaneously, they worked on the facade facing the front door, installing zinc cladding and placing insulation.**







**After receiving additional insulation materials by orders, the constructors began placing insulation not only on the facade but also within the interior walls of the apartments on the 1st floor. They then completed the wall structure by installing the second panels.**

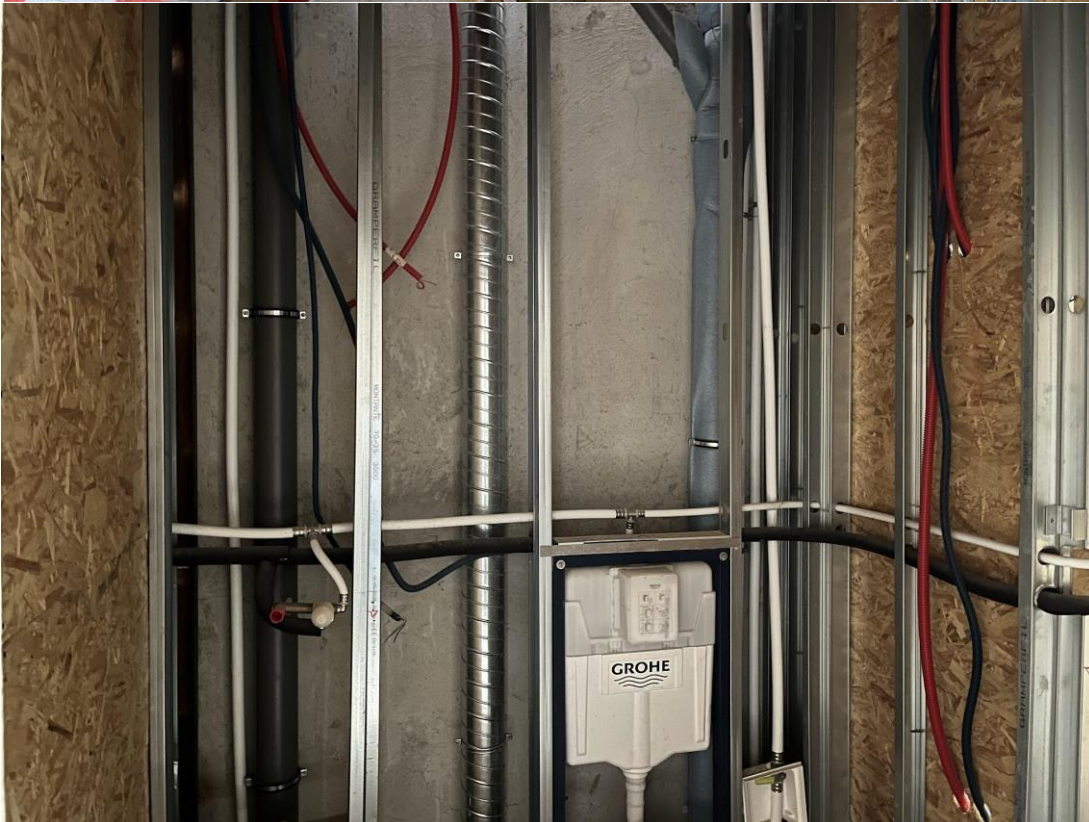











**Project:** Rua Nova do Loureiro 43-45, Lisboa

**Report Number:** Laurel - 27



**YAO TENG FGI**  
Property Development

---

**Following the work completed in April, the builders continued working on the electricity infrastructure installation on the 3rd floor and ground floor. They also progressed with the installation of a water piping system on the 3rd floor. At the end of May, they conducted a leakage test to ensure the water pipes were functioning properly. Additionally, they began installing infrastructure for the AC system.**
