

Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 26



YAO TENG FGI
Property Development

施工进度报告

月度报告 2024年5月

建筑商 NS Reformas, Construcción Y Trading S.L.U

当前进程

工程概述

1. 继续粉刷
2. 电力基础建设
3. 修复现有窗框
4. 浴室贴磁砖
5. 屋顶



工程照片



Project: Rua do Passadiço 55, Lisboa


Report Number: Passadiço - 26



YAO TENG FGI
Property Development





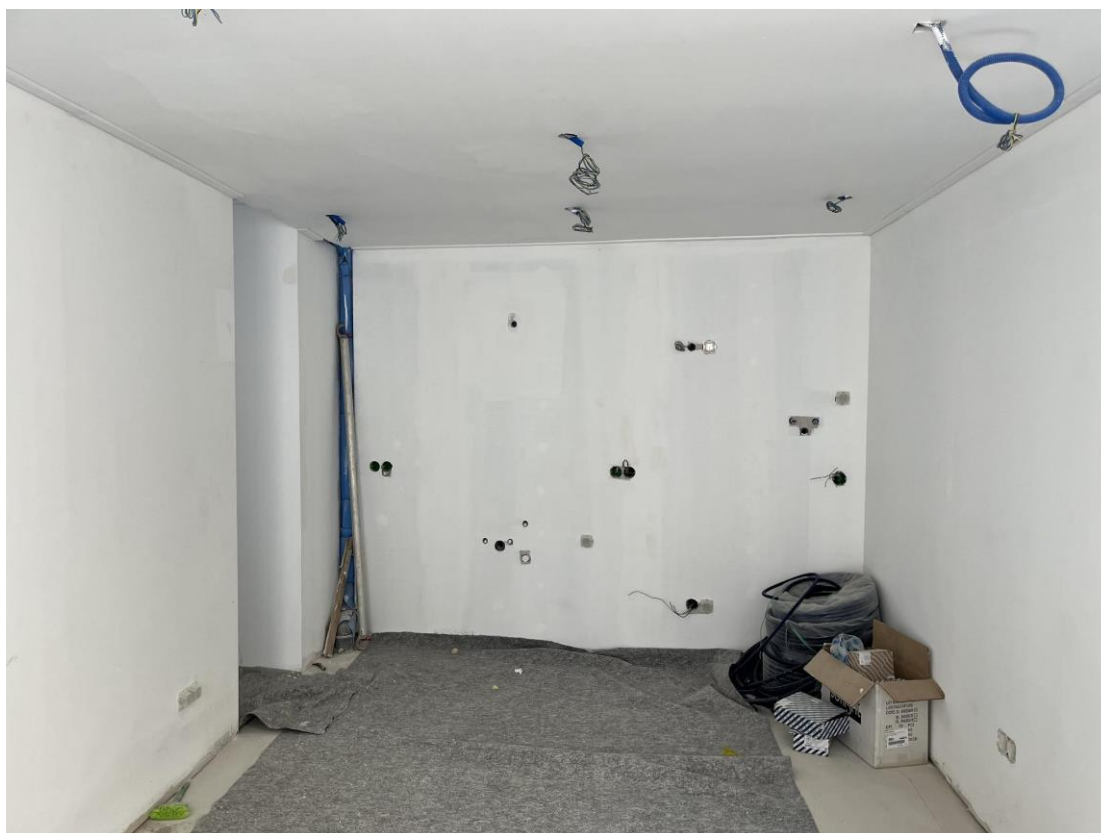



继四月的工作之后，建筑商们于五月继续努力地处理和填充底层墙壁和天花板的接缝。之后，他们开始粉刷墙壁和天花板。此外，建筑商也继续安装电线系统，包括在公寓内安装插头和插座。



Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 26



YAO TENG FGI
Property Development



Project: Rua do Passadiço 55, Lisboa

Report Number: Passadiço - 26



YAO TENG FGI
Property Development






正如先前的报告中所提到的，建筑商开始对底层以上公寓的浴室区域进行防水处理，为即将到来的瓷砖阶段做好准备。这个月，他们开始在浴室的地板和墙壁上铺设瓷砖。







根据葡萄牙修复工程的法规，必须保留建筑物的外观结构。建筑商于 5 月重点修复了现有的石窗框。进行这项重要工作是为了确保框架为计划于 6 月安装的新窗户做好适当准备。

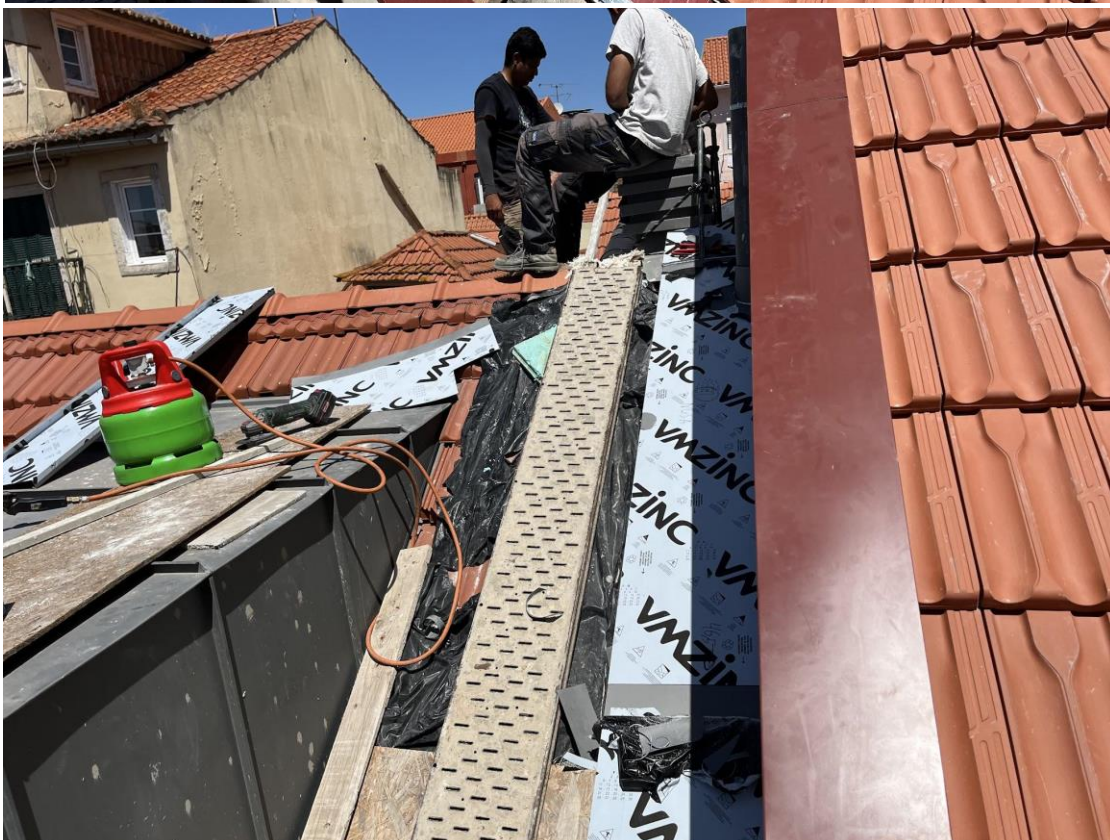



建筑商完成了屋顶瓦片的铺设，并完成了覆盖屋顶边缘部分的锌覆层的铺设。
