

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 26



**YAO TENG FGI**  
Property Development

---

## 施工進度報告

月度報告                      2024 年 5 月

建築商                              NS Reformas, Construcción Y Trading S.L.U

## 當前進程

工程概述

1. 繼續粉刷
2. 電力基礎建設
3. 修復現有窗框
4. 浴室貼磁磚
5. 屋頂



## 工程照片



**Project:** Rua do Passadiço 55, Lisboa


**Report Number:** Passadiço - 26



**YAO TENG FGI**  
Property Development





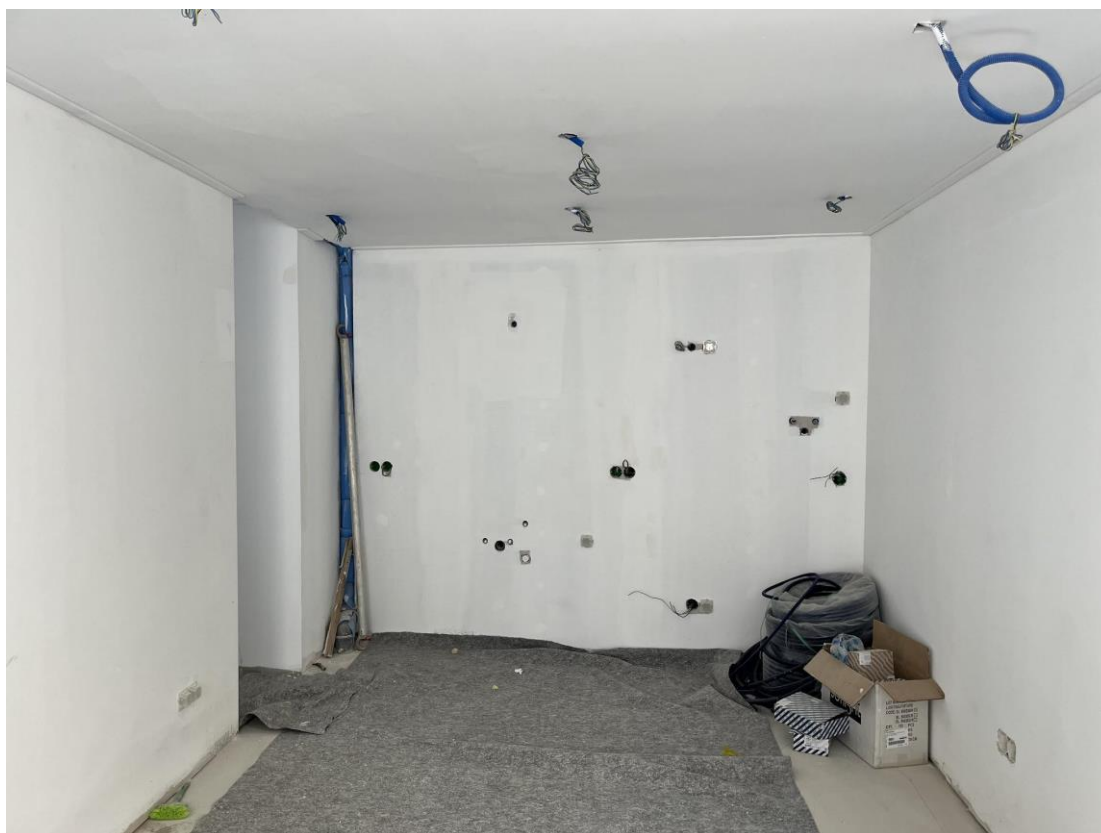

繼四月的工作之後，建築商們於五月繼續努力地處理和填充底層牆壁和天花板的接縫。之後，他們開始粉刷牆壁和天花板。此外，建築商也繼續安裝電線系統，包括在公寓內安裝插頭和插座。





**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 26



**YAO TENG FGI**  
Property Development








正如先前的報告中所提到的，建築商開始對底層以上公寓的浴室區域進行防水處理，為即將到來的瓷磚階段做好準備。這個月，他們開始在浴室的地板和牆壁上鋪設瓷磚。







根據葡萄牙修復工程的法規，必須保留建築物的外觀結構。建築商於 5 月重點修復了現有的石窗框。進行這項重要工作是為了確保框架為計劃於 6 月安裝的新窗戶做好適當準備。

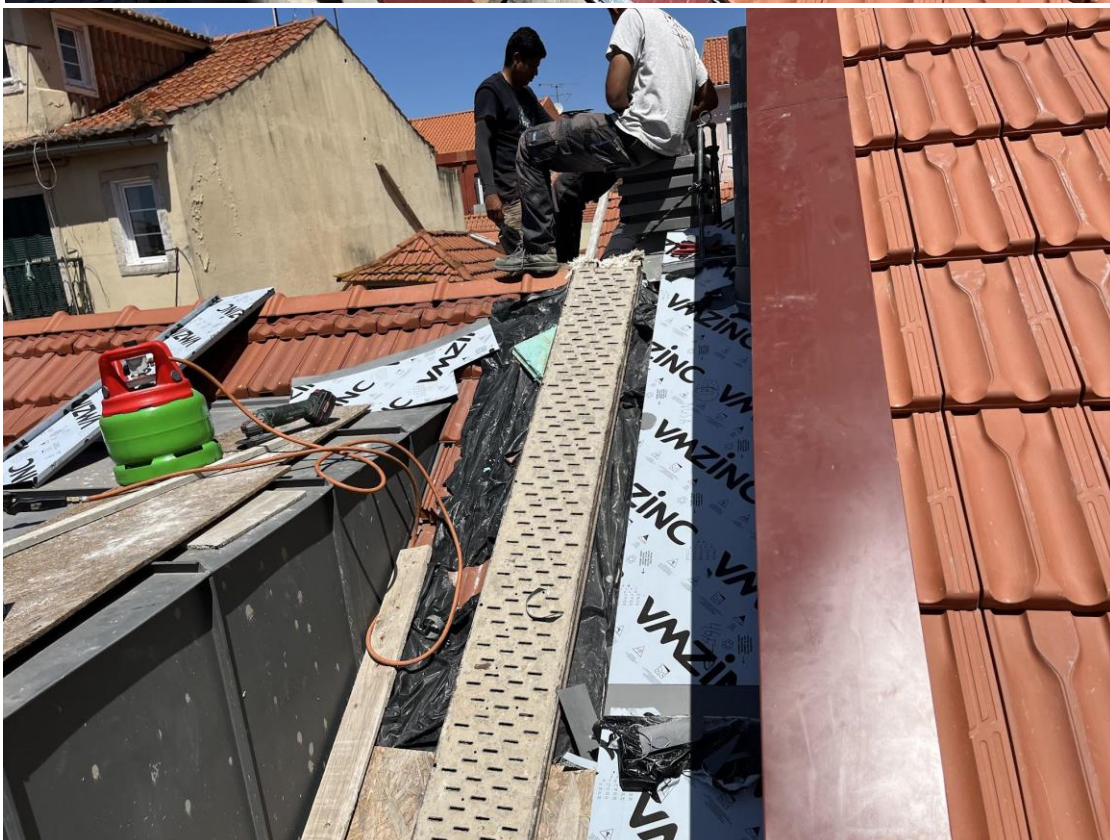

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 26



**YAO TENG FGI**  
Property Development



建築商完成了屋頂瓦片的鋪設，並完成了覆蓋屋頂邊緣部分的鋅覆層的鋪設。
