

**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23



**YAO TENG FGI**  
Property Development

---

## Construction Progress Report

**Monthly Period Reporting**

Start: Saturday, 01 June 2024

End: Sunday, 30 June 2024

**Builder**

LADRILLO S.A - Construção, Remodelações e Projecto

### Current Process

**Description of work**

1. Work on the roof

### Process Photos






**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23

**YAO TENG FGI**  
Property Development


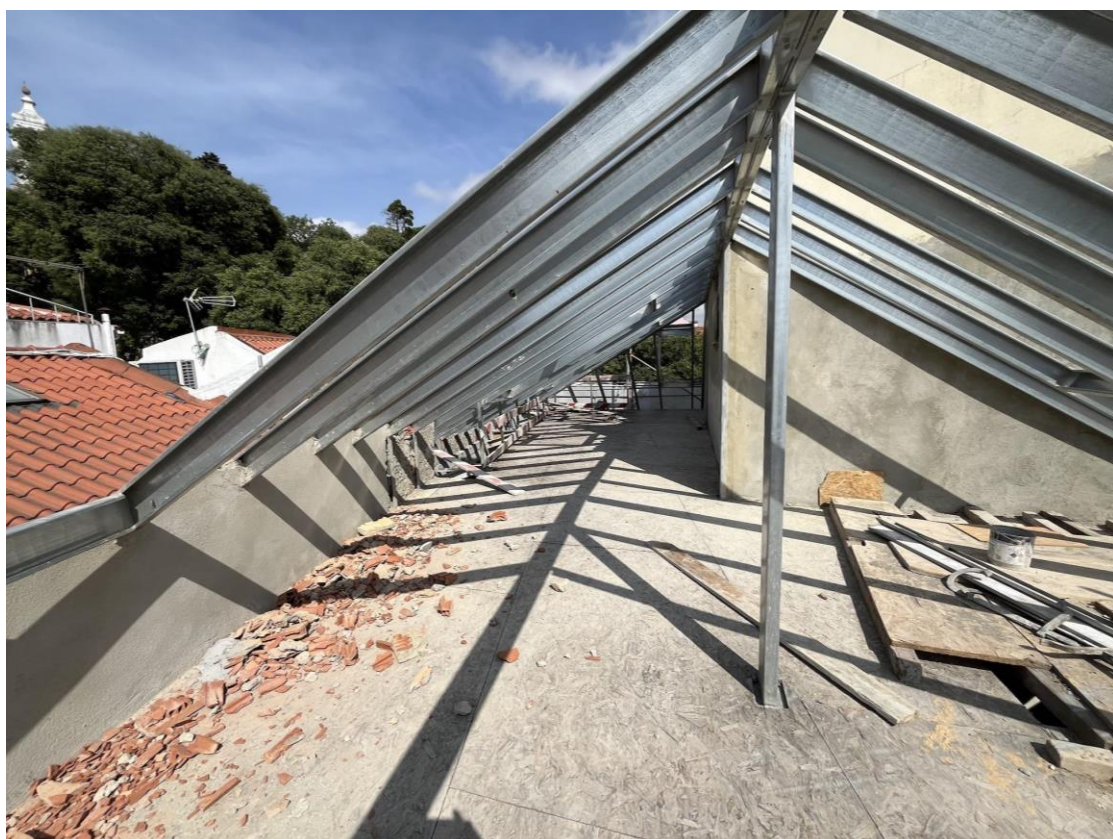




**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23

**YAO TENG FGI**  
Property Development

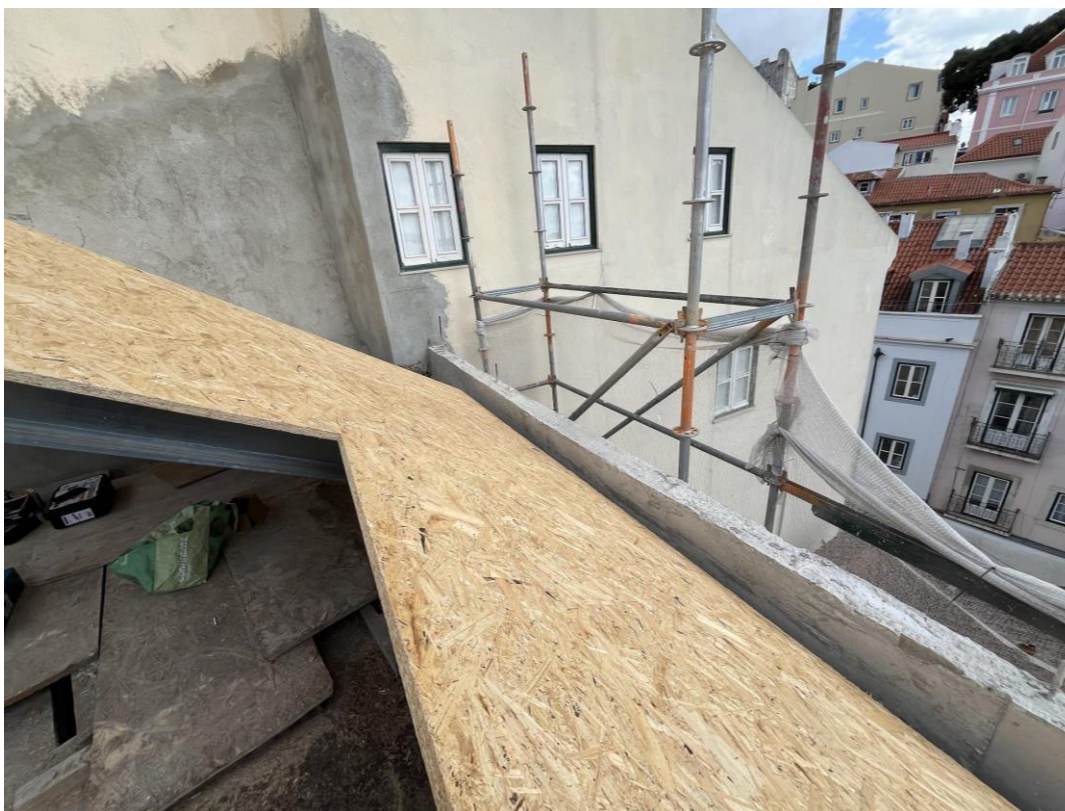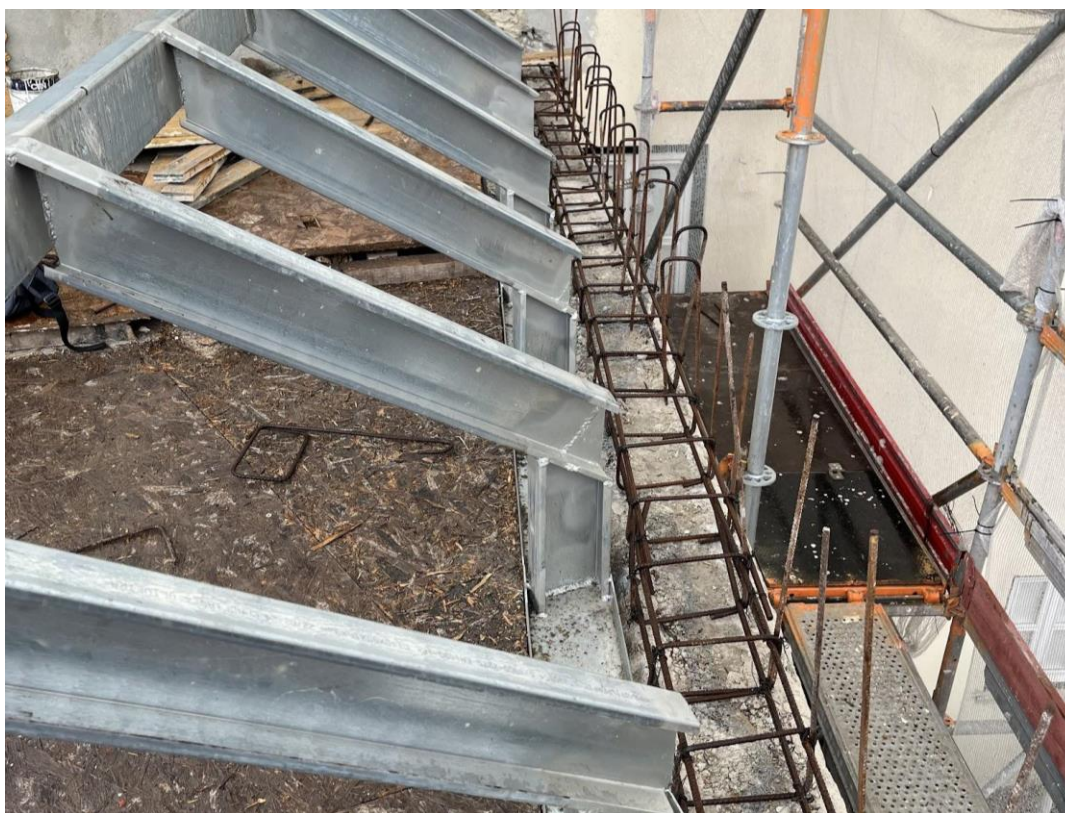



**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23

**YAO TENG FGI**  
Property Development





**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23

**YAO TENG FGI**  
Property Development





**Project:** Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

**Report Number:** Freiras - 23



**In June, the construction team concentrated on advancing the roof work. After assembling the roof steel structure, they proceeded with installing panels on it. By the end of the month, they started placing the sub-tiles on the panels in preparation for the final tiling.**

**Furthermore, they successfully built the surrounding walls along the roof edge, as well as the roof eaves and parapet.**
