

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

---

## 施工进度报告

月度报告                      2024 年 7 月

建筑商                          NS Reformas, Construcción Y Trading S.L.Uz

## 当前进程

工程概述

1. 放置地板保温层
2. 阳台贴磁砖
3. 粉刷墙壁

## 工程照片

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27




**YAO TENG FGI**  
Property Development





依照 7 月的工作议程，地板保温材料的安装工作于 7 月开始，从三楼开始，往下进行到底层。所使用的绝缘材料是软木，因其隔音和隔热性能而被选择。到月底，团队精心完成了二楼和三楼的安装工作。

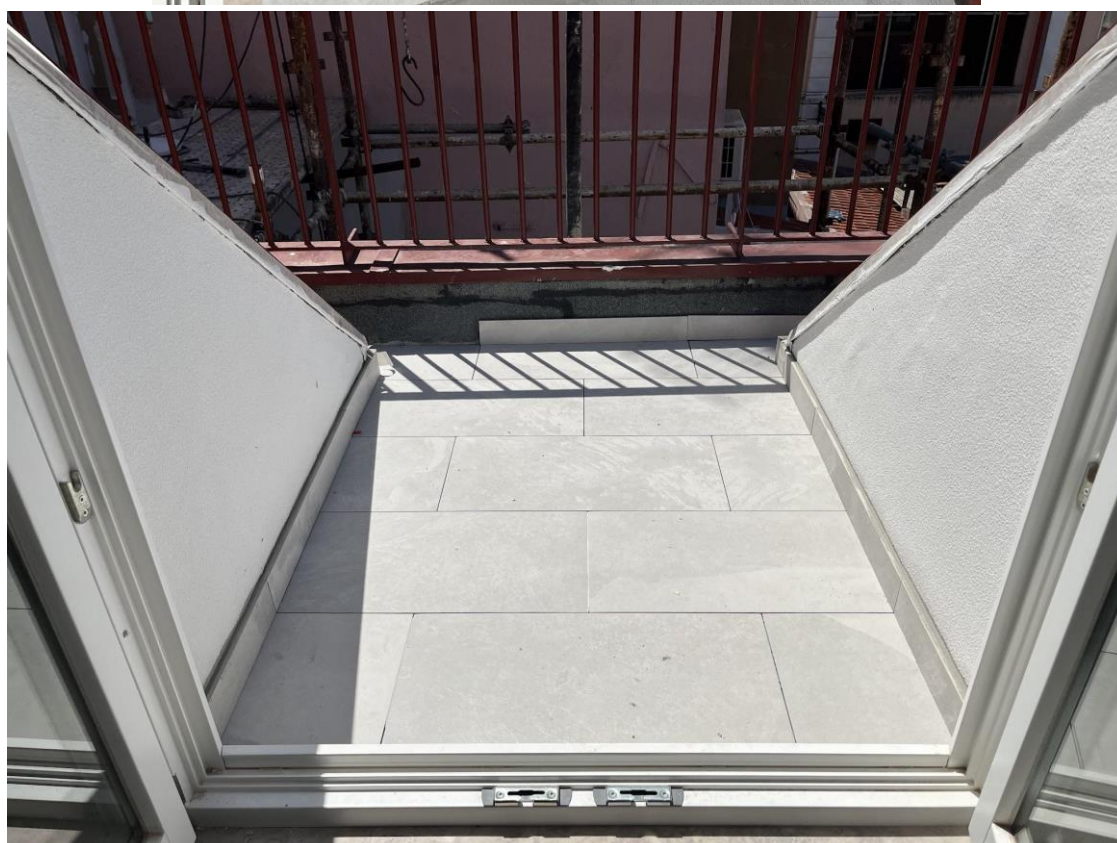


**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

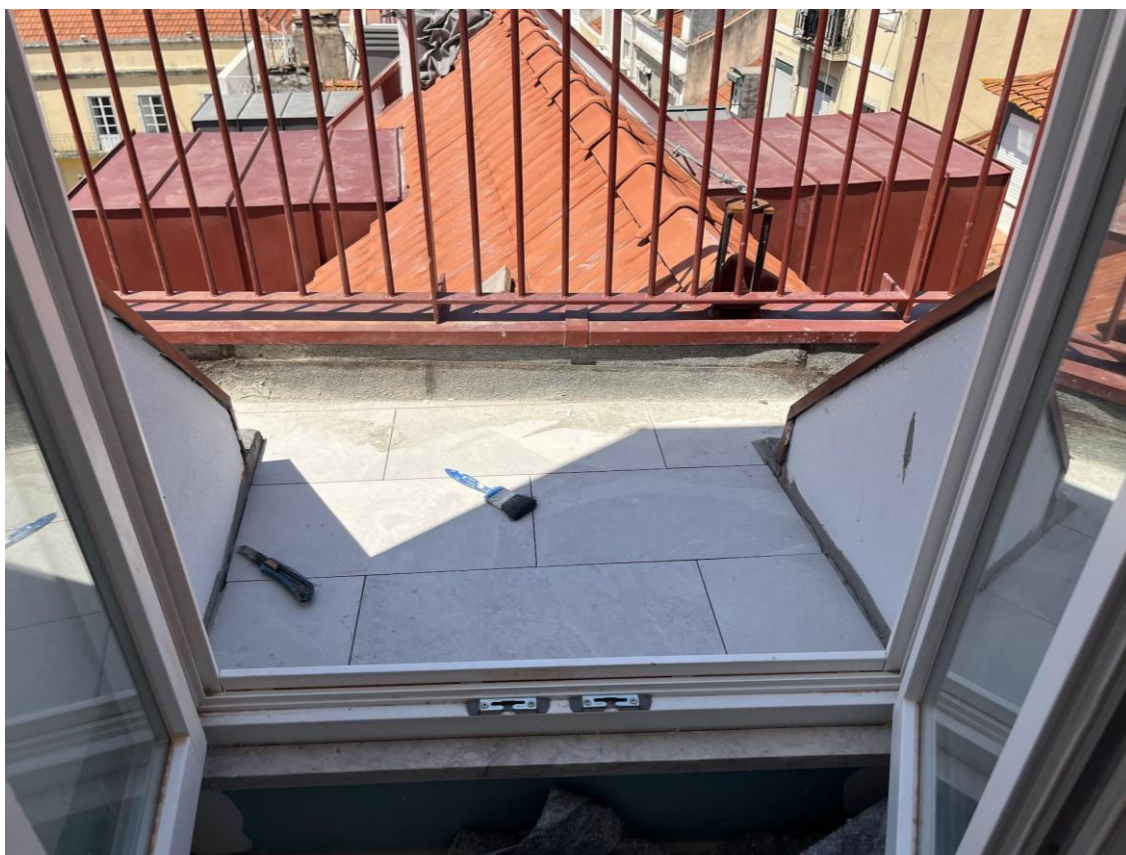







同时，施工队正在平整阳台地板，准备贴上磁砖。7月，磁砖交付后，他们开始在阳台上贴上磁砖。





**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development





**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

---

油漆工作于七月继续进行，施工团队的重点是公寓的内墙。此外，根据许可计划，他们开始将外墙漆成米色。
