

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

---

## Construction Progress Report

**Monthly Period Reporting**

Start: Monday, 01 July 2024    End: Wednesday, 31 July 2024

**Builder**

NS Reformas, Construcción Y Trading S.L.U

### Current Process

**Description of work**

1. Place floor insulation
2. Tile the balconies
3. Paint the walls

### Process Photos



**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27




**YAO TENG FGI**  
Property Development





**Following the work agenda, in July, the installation of flooring insulation commenced in July, starting from the 3rd floor and progressing downward to the ground floor. The insulation material used is cork, chosen for its soundproofing and thermal insulation properties. By the end of the month, the team had meticulously completed the installation on both the 2nd and 3rd floors.**

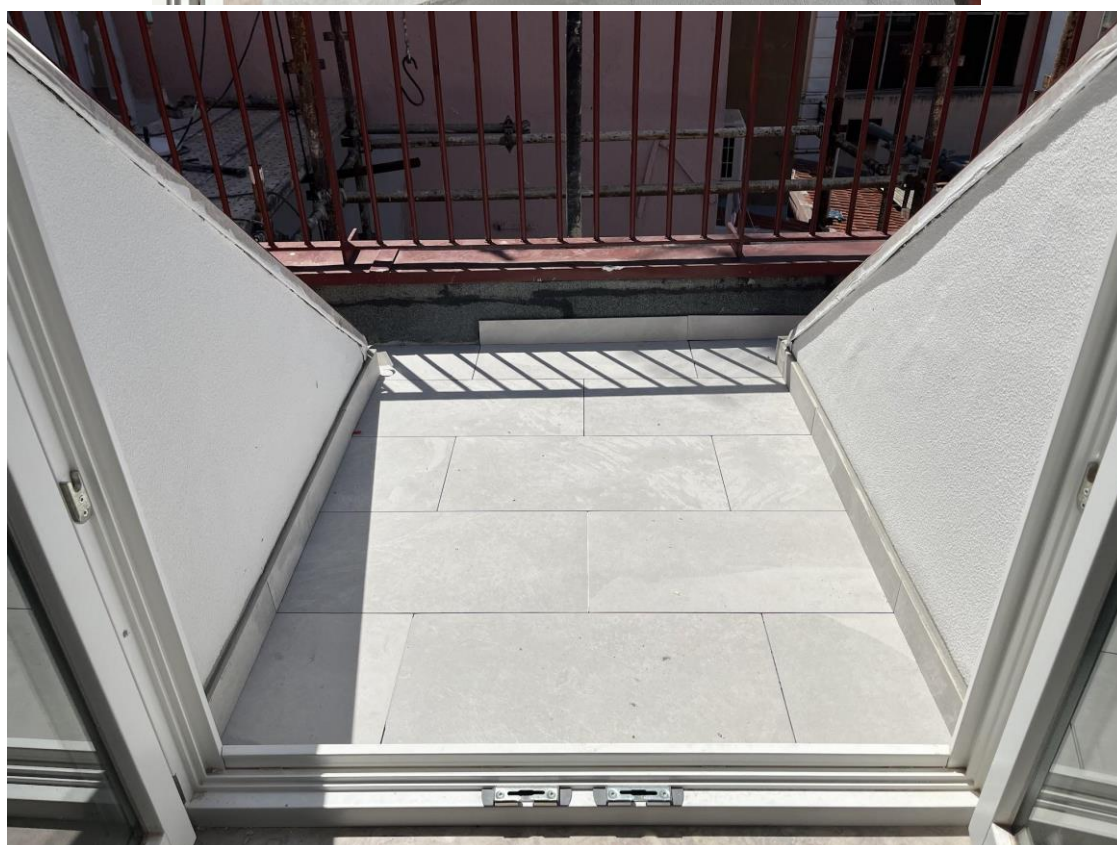


**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

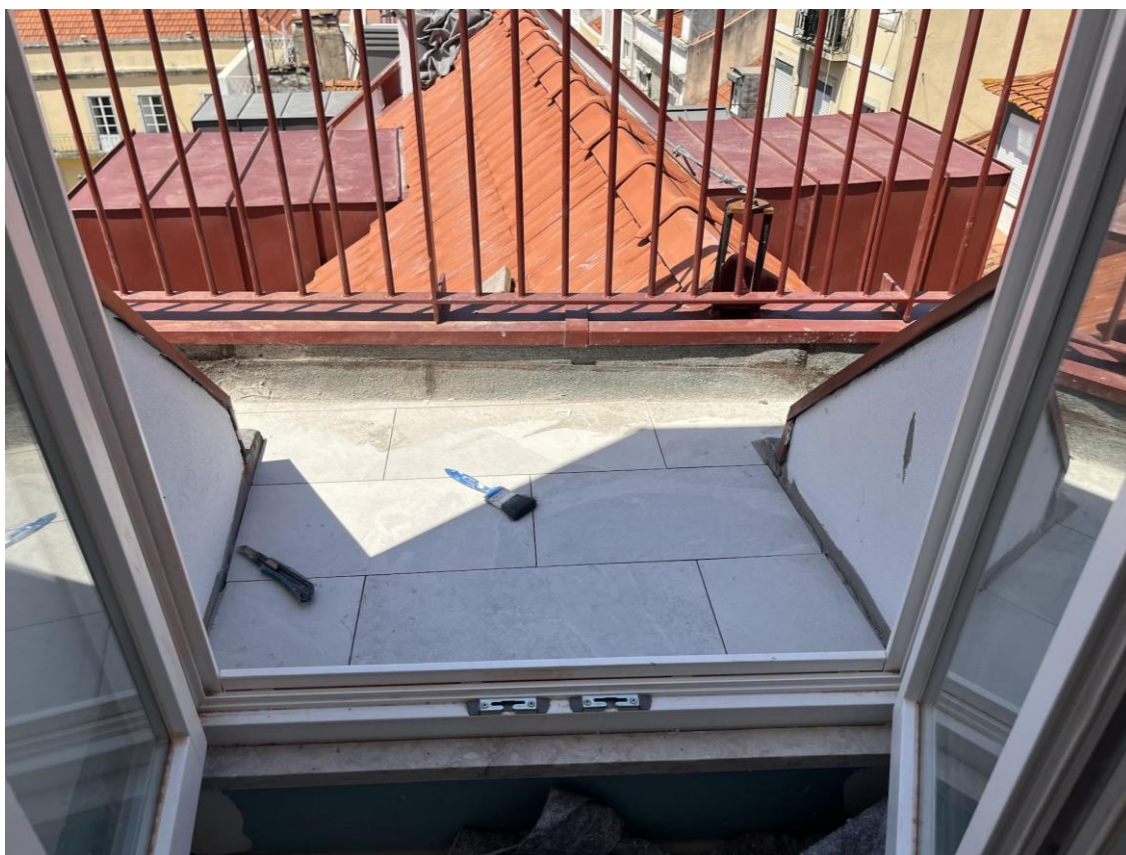







**Meanwhile, the construction team was leveling the balcony floors in preparation for tiling. In July, after the tiles were delivered, they began the tiling process on the balconies.**






**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development



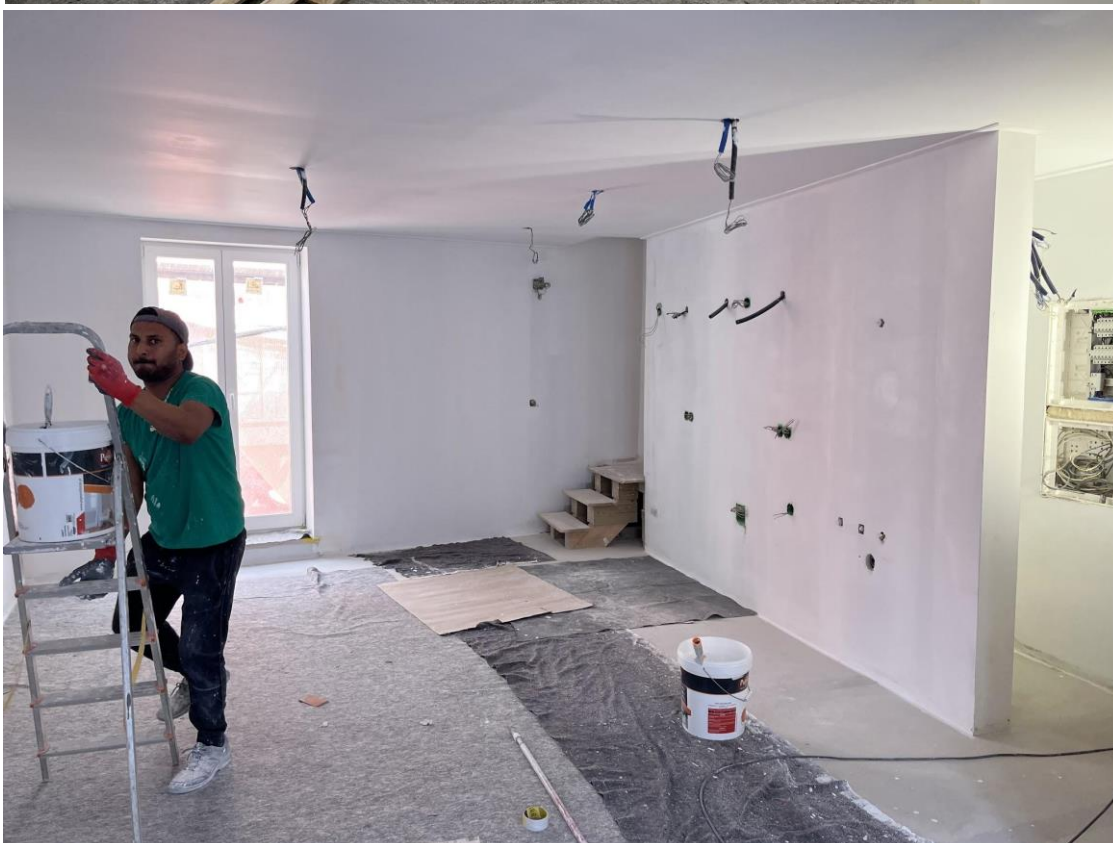

**Project:** Rua do Passadiço 55, Lisboa

**Report Number:** Passadiço - 27



**YAO TENG FGI**  
Property Development

---

**Painting work continued in July, with the construction team focusing on the interior walls of the apartments. Additionally, they began painting the facade in beige, in accordance with the licensing plan.**
