

Project: Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

Report Number: Freiras - 24



YAO TENG FGI
Property Development

Construction Progress Report

Monthly Period Reporting

Start: Monday, 01 July 2024

End: Saturday, 31 August 2024

Builder

LADRILLO S.A - Construção, Remodelações e Projecto

Current Process

Description of work

1. Finish roof sub-tiling
2. Assemble 1st-floor pavement steel structure
3. Place insulation of the exterior walls

Process Photos















As mentioned in the previous report, the construction team was focused on the roof. They successfully completed the installation of panels on the roof's steel structure and proceeded to place the sub-tiling materials on these panels in preparation for the final tiling in July and August. Following this, they began tiling on the eaves in August.




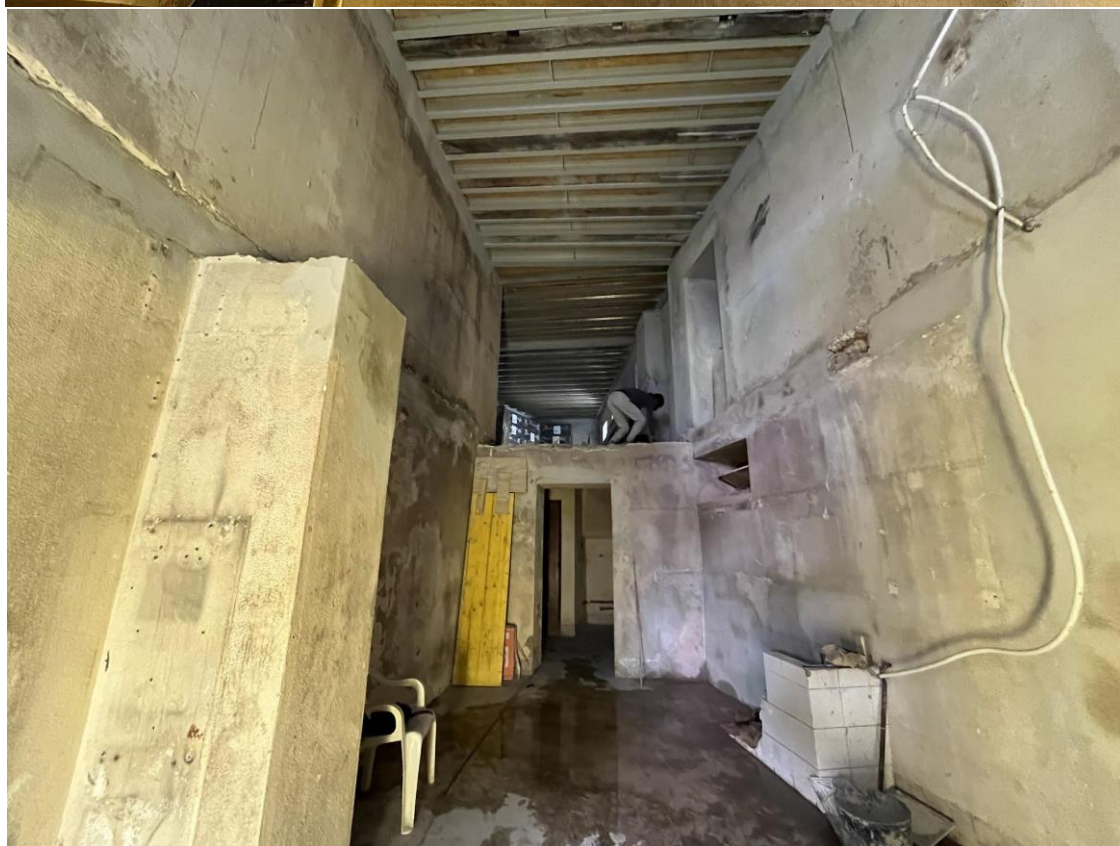

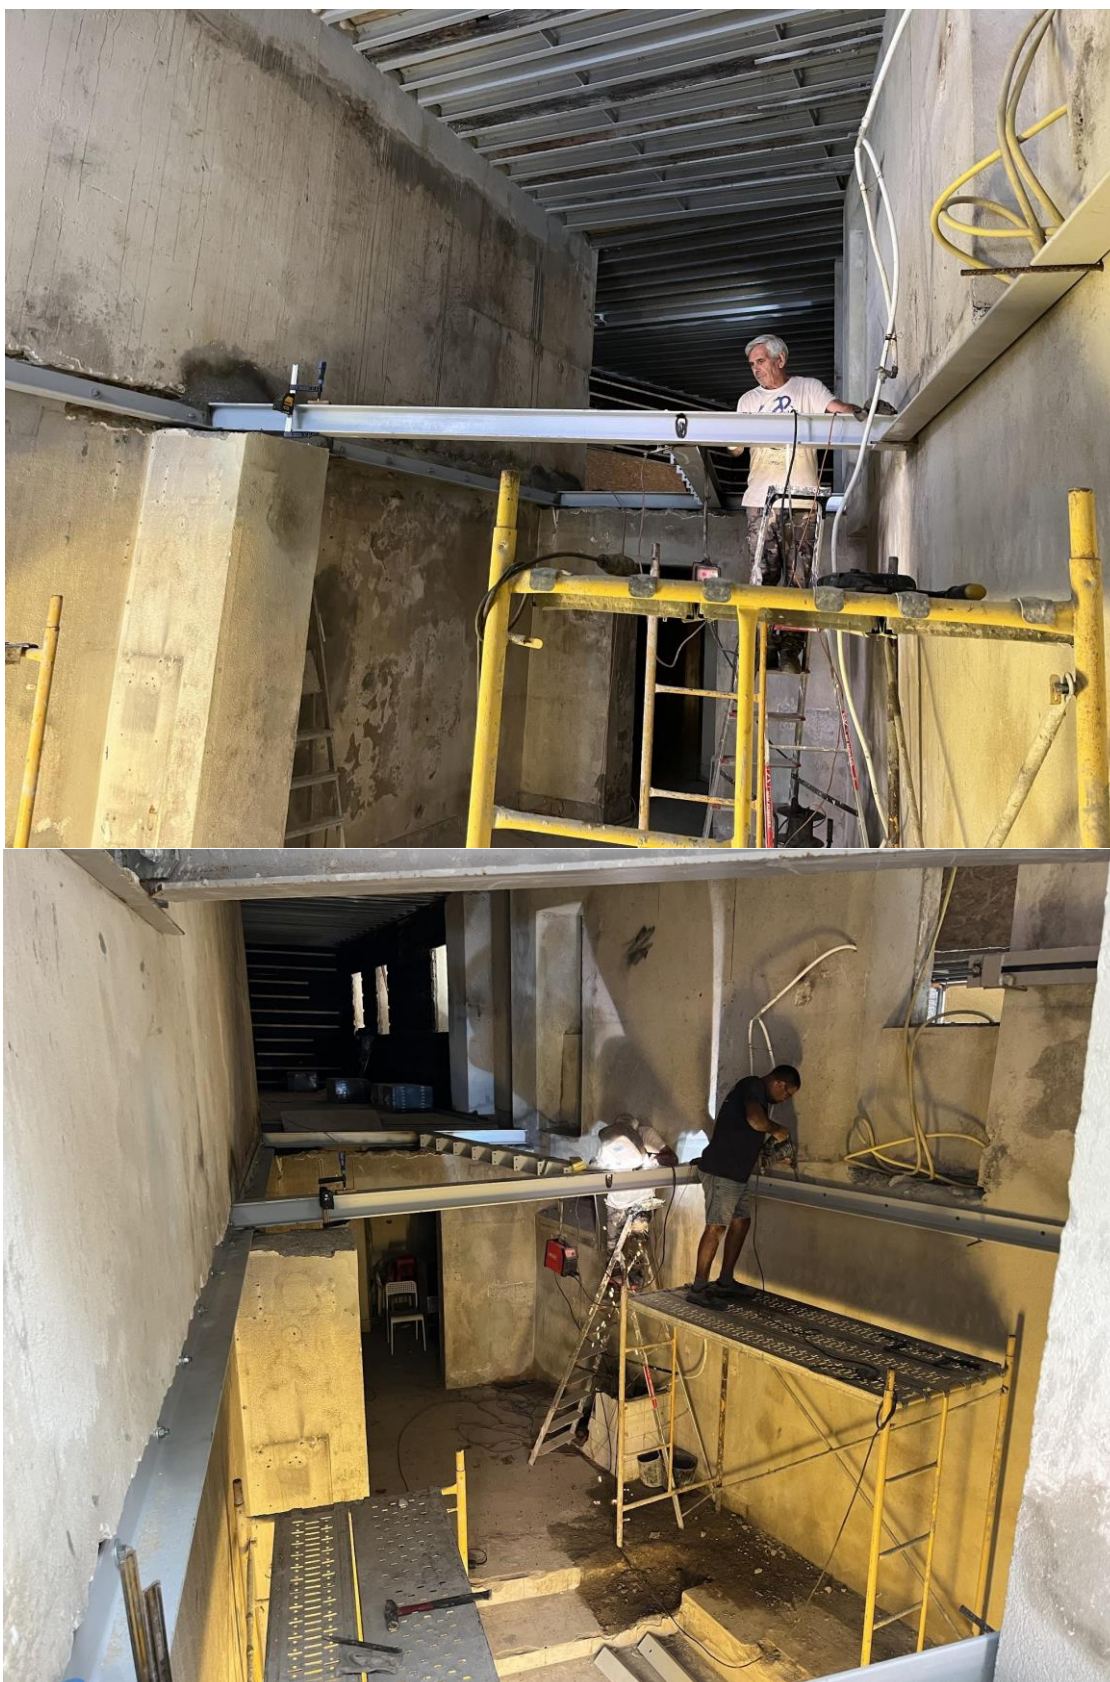

In August, the construction team demolished the remaining non-structural sections of the ground floor pavement and walls. Following this, they commenced the assembly of the steel structure for the remaining pavement on the first floor.



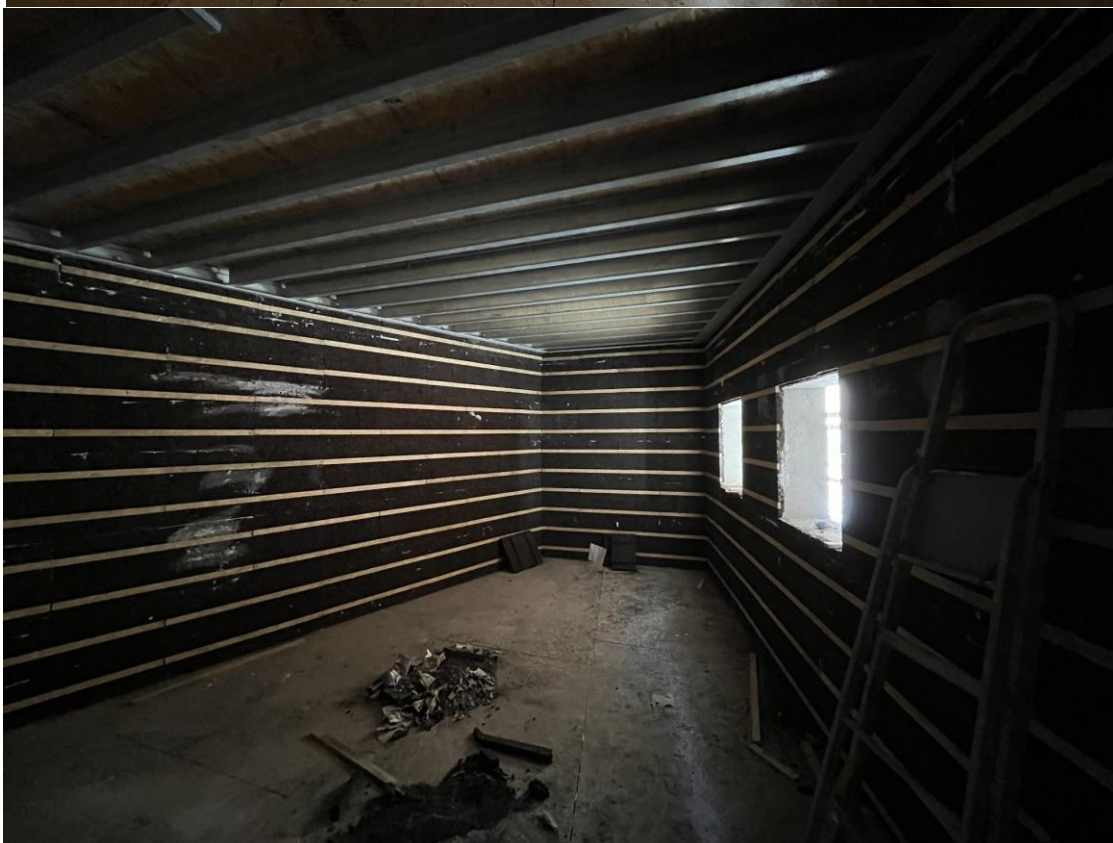



Project: Largo Rodrigues de Freitas no 4 e 5 e Beco da Lage no 4, 1100-455 Lisboa

Report Number: Freiras - 24



Meanwhile, after the insulation materials were delivered to the job site at the end of July, the construction team began installing insulation on the exterior walls. The installation was carried out sequentially on the 1st, 2nd, and 3rd floors to enhance the building's heat insulation and soundproofing.
